
Date : 12/08/22.

MON TUE WED THU FRI SAT SUN

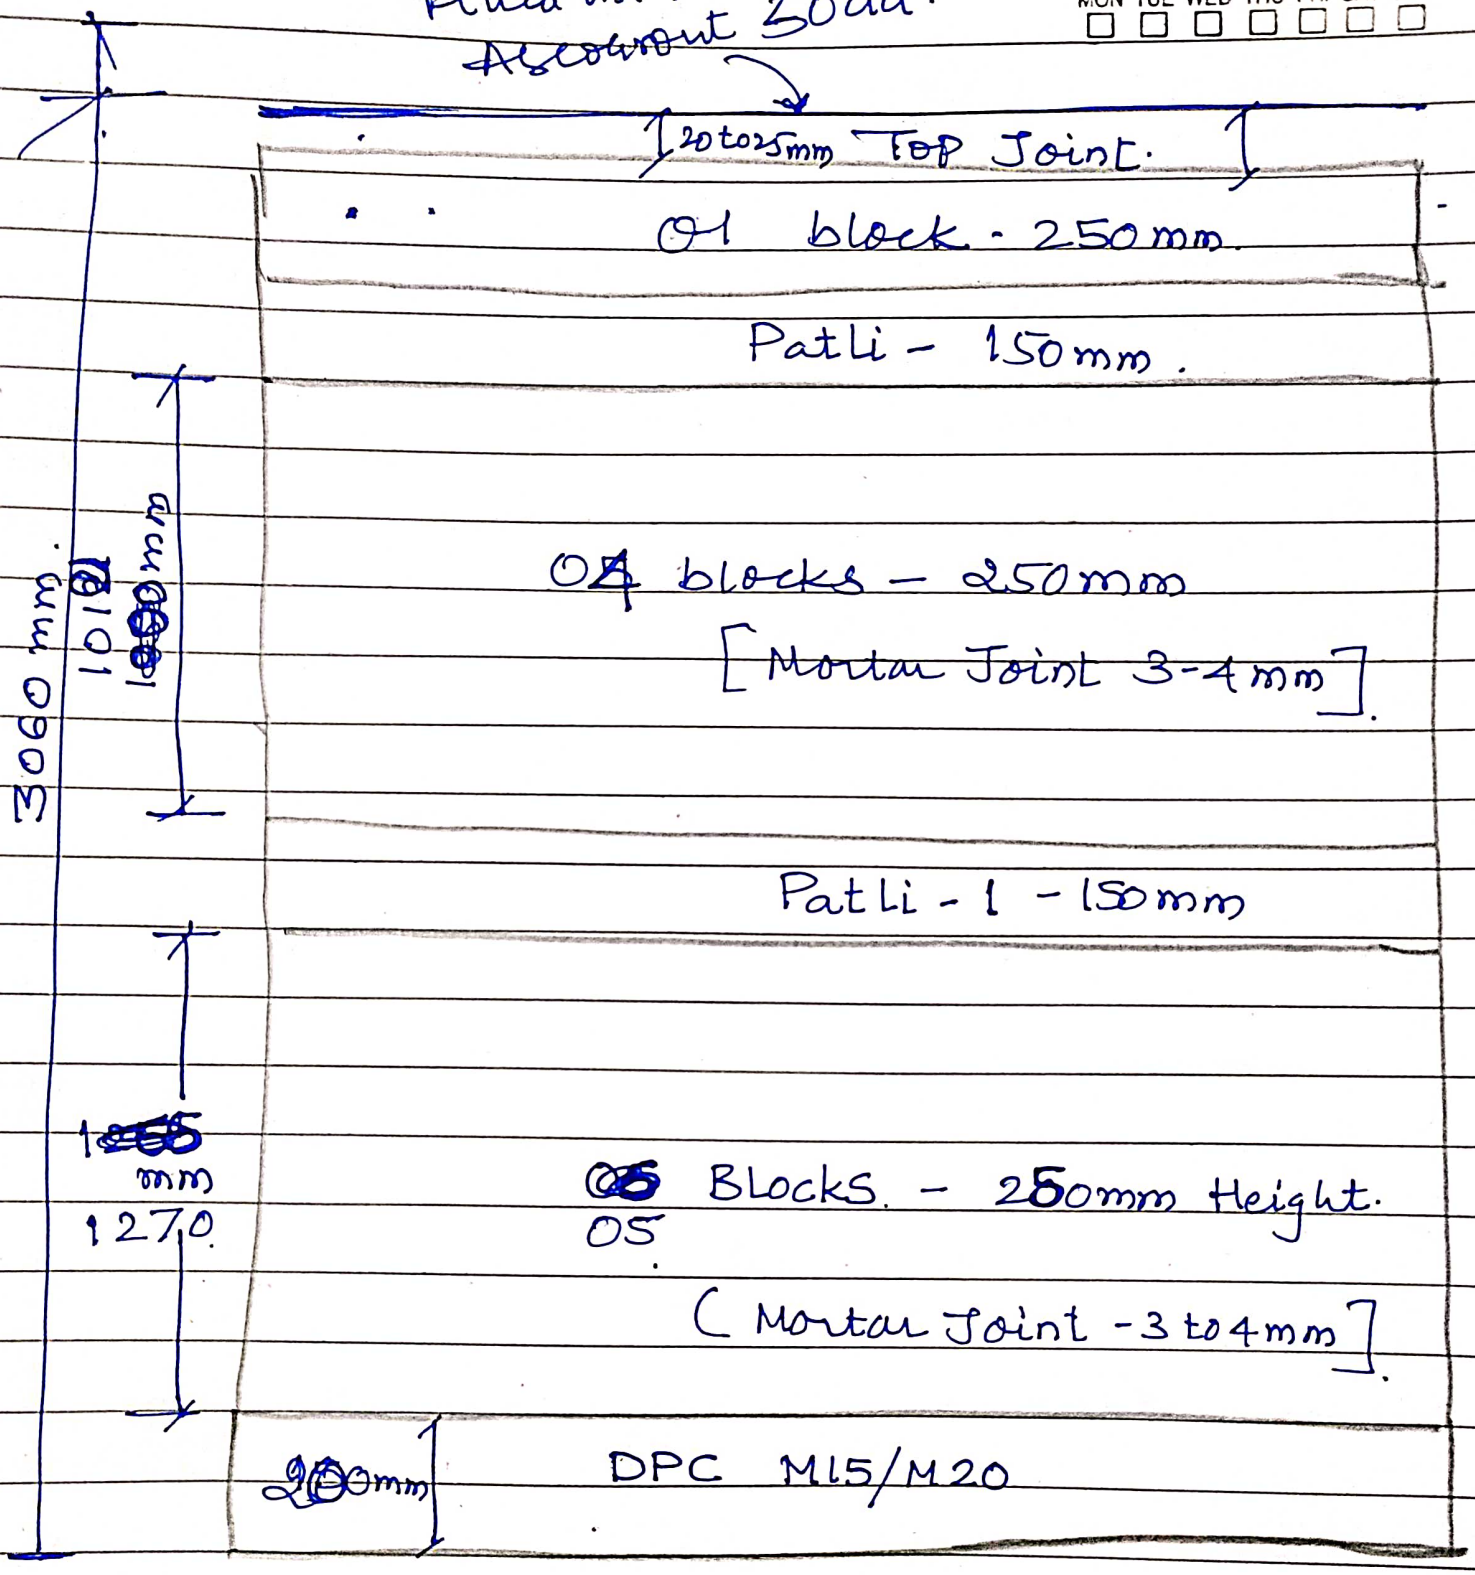


ELEVATION OF BLOCKWALL AT SCHOOL AT UPPER THANE [AAC Block].

For 3585mm Height - 03 block Raw at top.

Date :...12/08/22...

MON TUE WED THU FRI SAT SUN



35 to 40mm Top Joint.

03 blocks - 600mm

Patli - 110 mm.

05 blocks } Solid blocks.
(200 x 5) - 1m.

Patli - 110 mm.

05 blocks - Solid block
190mm
+10 mm Mortar Joint.
200mm.

DPC = 200 mm.

ELEVATION OF BLOCKWORK AT SCHOOL AT UPPER THANE (Solid block)
