

Acme Ozone - Initial Feedback/Comments

1 Shops Area - Transfer need to be eliminated

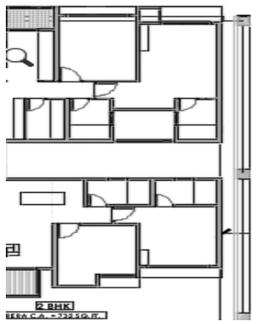


2

West side - column/walls interfere with driveway at parking levels - about 4.5m cantilever
Transfer eed to be eliminated




3

8 ft cantilever deck from transfer/flare columns
is not recommended




4 about 4m cantilver with 1m backs span not recommended
Transfer girder at stilt level is possible but not preferred.

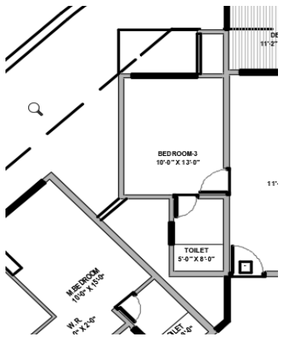

5

Separation/expansion Joint is mandatory

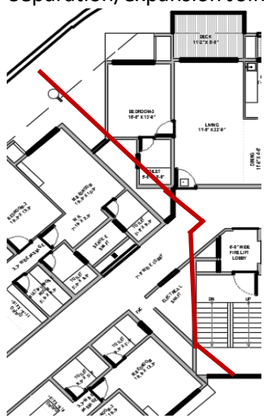

6

Stair core at typical level interfere with driveway below
Transfer is not recommended.

