KAPADIA ASSOCIATES
DESIGN LLP

112 – 114, Peninsula Center, Dr. S. S. Rao Road, Off S. S. Rao Road, Parel East, Mumbai 400012. Tel.: 6660 2838 Fax: 6660 2844

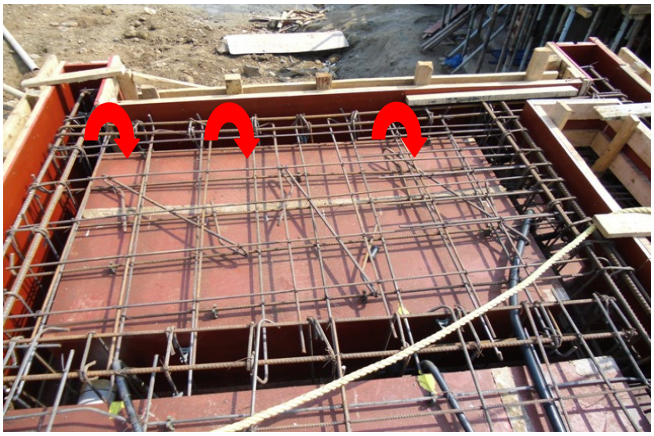
STATUS REPORT

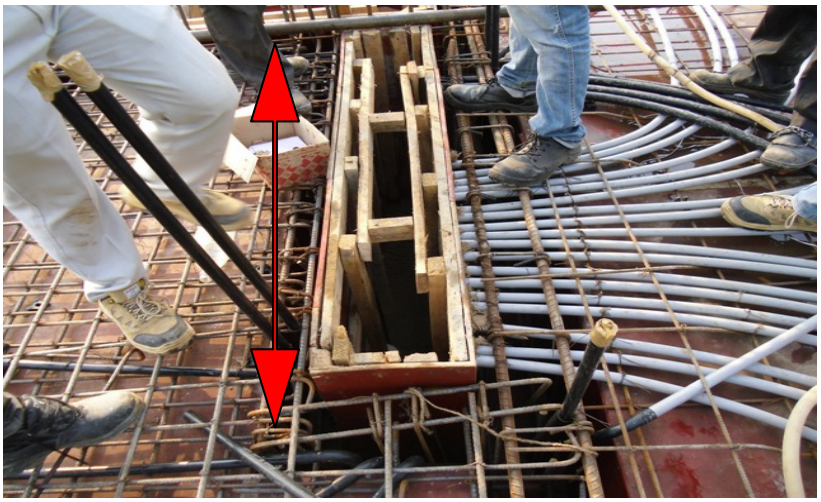
To Venkatesh. Date:-26-Nov-2014.

From Ashok Sandipamu.

Project Lodha-Palava-Koni.

Subject Slab Report for Primia-H wing 2nd floor, conducted on 25-Nov-2014.

Sr.	Area / Location	Images	Comments / Observation	Recommendation
1	Terrace / Balcony & service area.		M.S insert plate for railing is missing / not provided.	To be provide as per drawings. Drawings are issued on 19/11/2014 from Lodha H.O.
2	Terrace slab @ unit 01		Cut out is missing at corner of terrace slab	To be provide as per drawings.

Sr.	Area / Location	Images	Comments / Observation	Recommendation
3	Kitchen utility @ unit 04		Beam width varies 105mm to 125 mm.	110 mm To be provide as per drawings.
4	Terrace slab @ unit 05		No alignment between beam face and cut out	To be rectified.
5	Electrical cut out @ staircase 01		Work in progress	To be provide as per drawings.

Some of the snaps taken from Primia H wing & Elite F wing after casting Slab at ground floor & first floor.

Sr.	Area / Location	Images	Comments / Observation	Recommendation
1	Prima-H -wing Toilet @ 03 & 04		Instance of sagging	Avoid this kind of workmanship.
2	Prima-H -wing Staircase cut out		No beam Alignment	Maintain proper alignment

Sr.	Area / Location	Images	Comments / Observation	Recommendation
3	Prima- H -wing M.bed Room @ unit 03 & 04		Beam bulged	Avoid beam bulge
4	Elite- F -wing. Stair case passage.		Touch up is not done properly	Touch up the column with, rich mix / same grade of the column

Sr.	Area / Location	Images	Comments / Observation	Recommendation
5	Elite- F -wing. Bed-room		Touch up is not done properly	Avoid huge honey comb. Touch up the column with, rich mix.

Note:-Site to proceed with RCC works after addressing the comments.

Checked & observed on site by:-
Gauri Kulkarni - Lodha.
Jayesh - Lodha.
Ashok Sandipamu - KAPL.
