
PREMIER SALES GALLERY

SITE VISIT ON 2021-11-29



Paint was looking patchy
Also screw marked were visible
To be sealed with matching paint

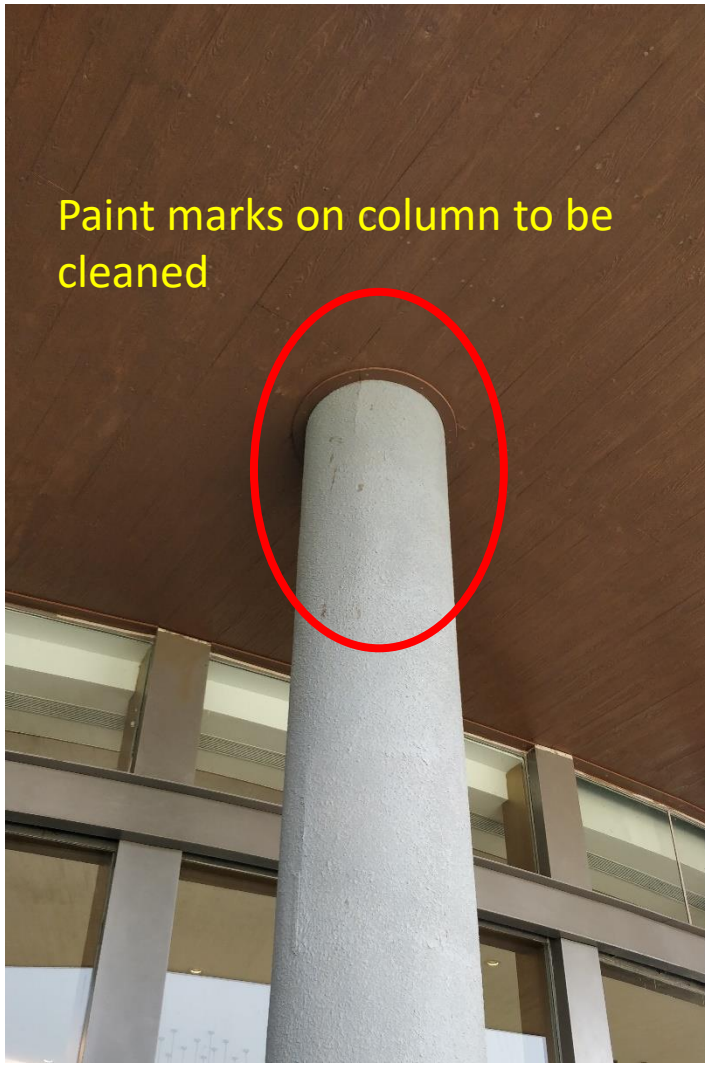

Gap to be filled with bison board/ façade flashing



Paint to be finished properly



Colour of the joint to be matching with cladding
To minimised the visibility.




Frame welding to be cleaned and polished finished with RAL 7024/ matching to the façade cladding
Cladding has been broken at the tie member junction
Glass to be cleaned







Ideally same cladding and fin to be continued till floor

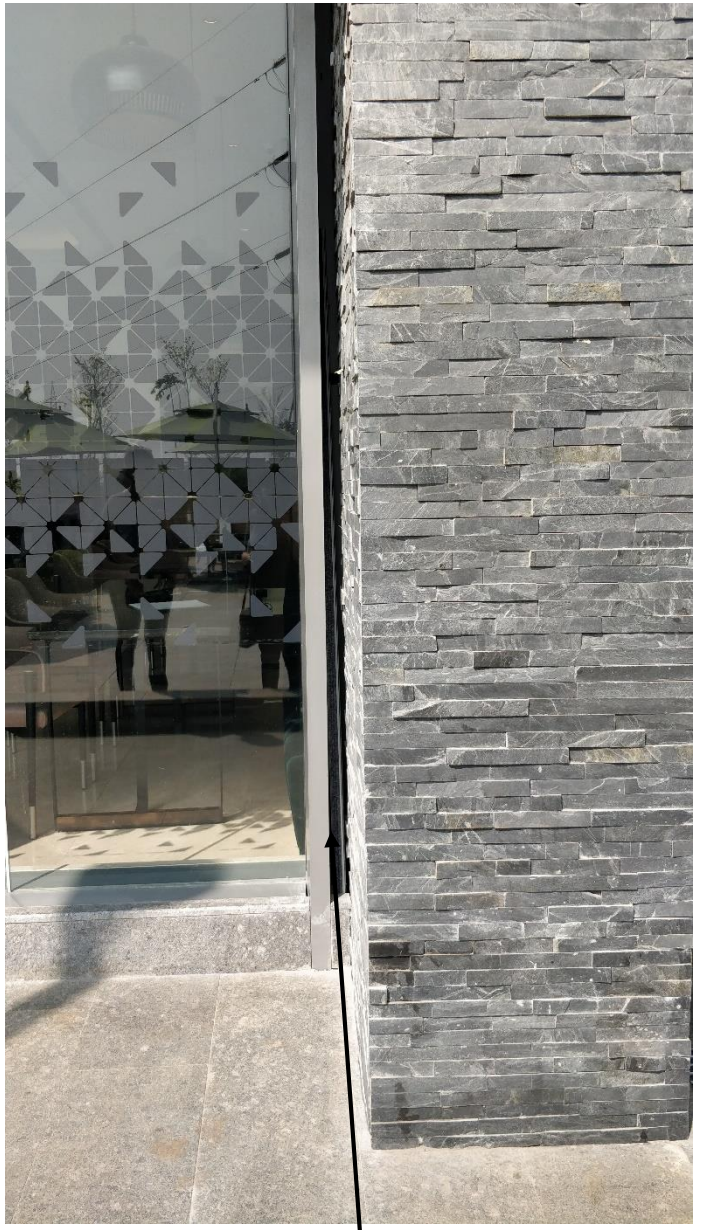

Gap to be cleaned and maintained properly.
Façade team to confirmed if that can be sealed/ filled



Stain marking to be cleaned



This walls to be painted with same shade of exterior round columns





To be packed with exterior grade bison board finished with paint





All these base stone to be cleaned and painted







Pebbles are missing at rear side. Refer Landscape drawing for the extent



Offset at the bottom of the cladding to be min. tile thickness only. Please rectify.
Plinth protection to be continued all across.

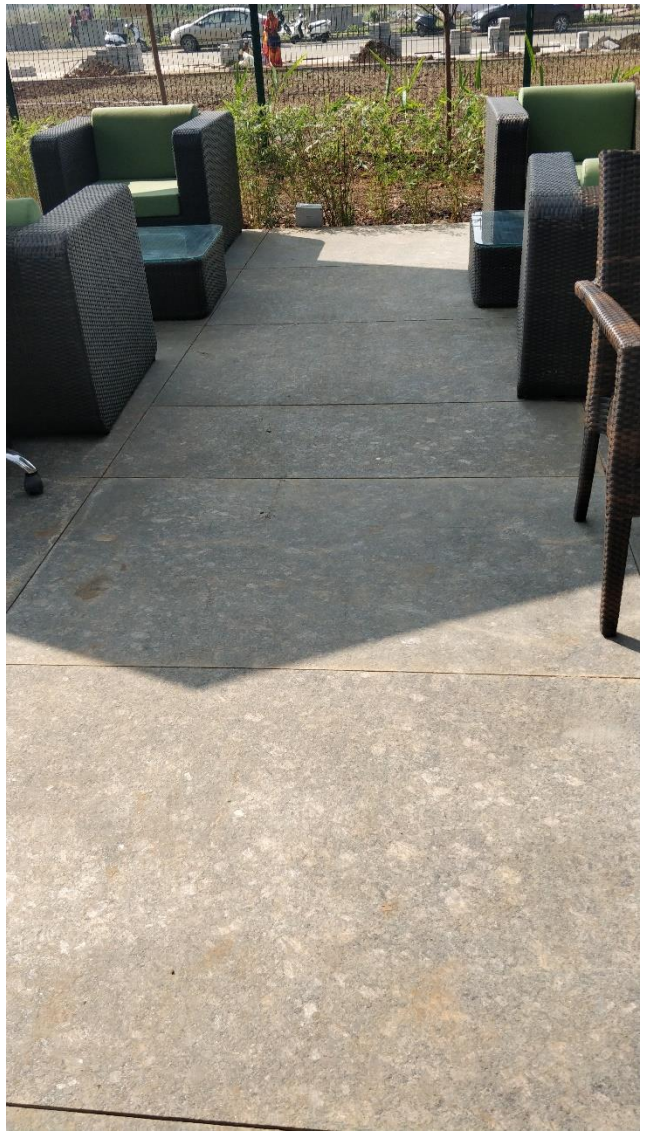

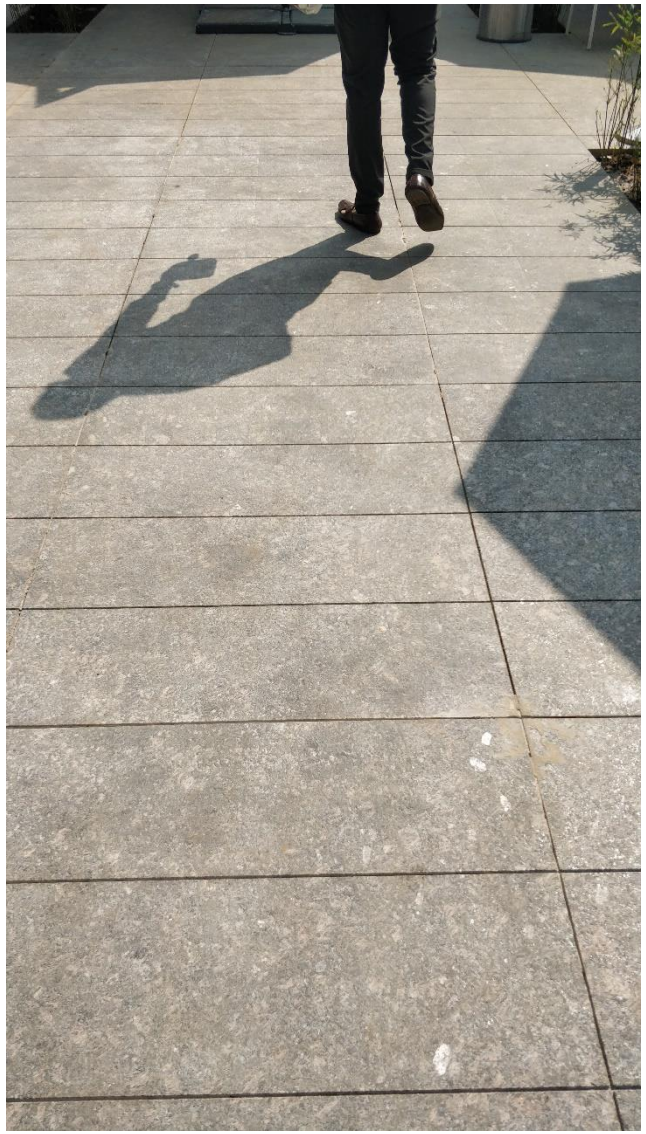

Tile joints are not as per drawing. Please follow flooring pattern as per drawing.
Joints to be filled with grout matching to the granite.



Lawn to be added between the gaps of the steps



Gutter is visible from the distance,
please rectify.



Edge detail given but not executed , hence border started cracking. please rectify.





Cracks started developing in the parking area



Broken plinth protection tile to be replaced.



Civil work to be finished and painted around the pipe. Pipe to be concealed in the soil and plinth protection tile to be continued.




Aerator pipe need to be below water level



Soil alignment to be same across the plinth protection line.
Drop of plinth protection is missing



This are plantation is pending.

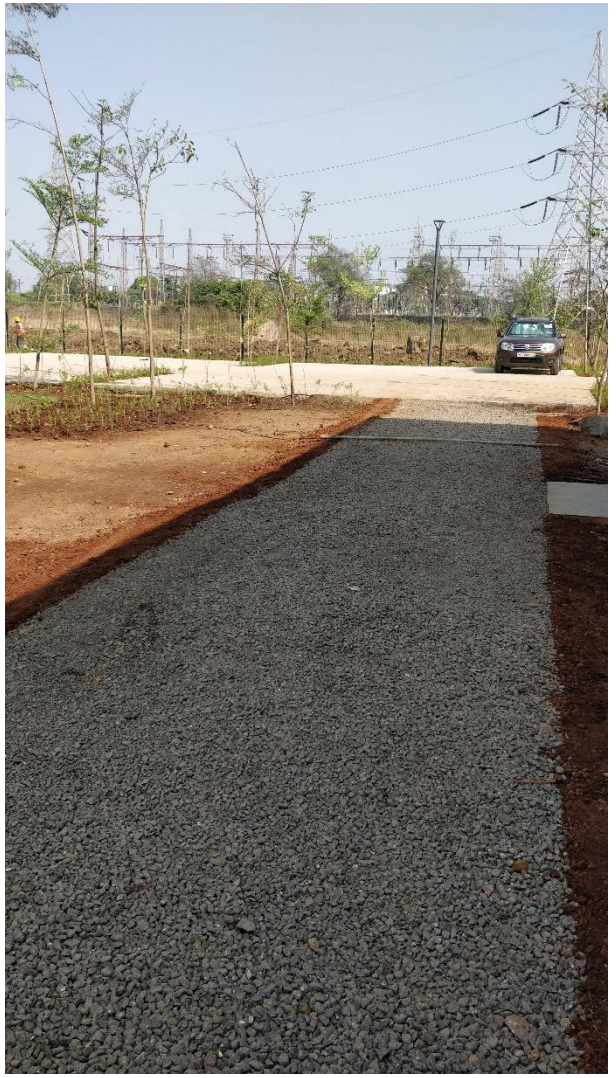

Charu walkway and plantation is pending.

THANKS

IGNORE IF ALREADY DONE.
